

**THE CORPORATION OF TAY VALLEY TOWNSHIP
REQUEST FOR TENDER**

UPPER SCOTCH LINE CULVERT REPLACEMENT

CONTRACT #2018-PW-013

ADDENDUM NO. 3

**THIS ADDENDUM SHALL BE INCORPORATED INTO THE TENDER PACKAGE
AND SHALL FORM A PART OF THE CONTRACT DOCUMENTS**

Date Issued: September 27, 2018
Issued By: Amanda Mabo, Clerk

Please note the following changes, corrections, additions, deletions, information and/or instructions in connection with the Tender Package. Failure to acknowledge receipt of this Addendum as per Part "A" – Information to Bidders may render your submission non-responsive.

This addendum is to address the following clarification:

Question:

Due to the availability and the subsequent turn-around time of ordering the SPCSPA, we have concerns with the project completion date of November 2, 2018. Can the project completion date be extended to allow for adequate time for shop drawings, approvals, manufacturing and the polymer coating of the SPCSPA?



Answer:

The project completion date is extended until November 30, 2018.

Clarification:

Please find attached borehole logs for this project.

Amanda Mabo, Clerk
clerk@tayvalleytp.ca

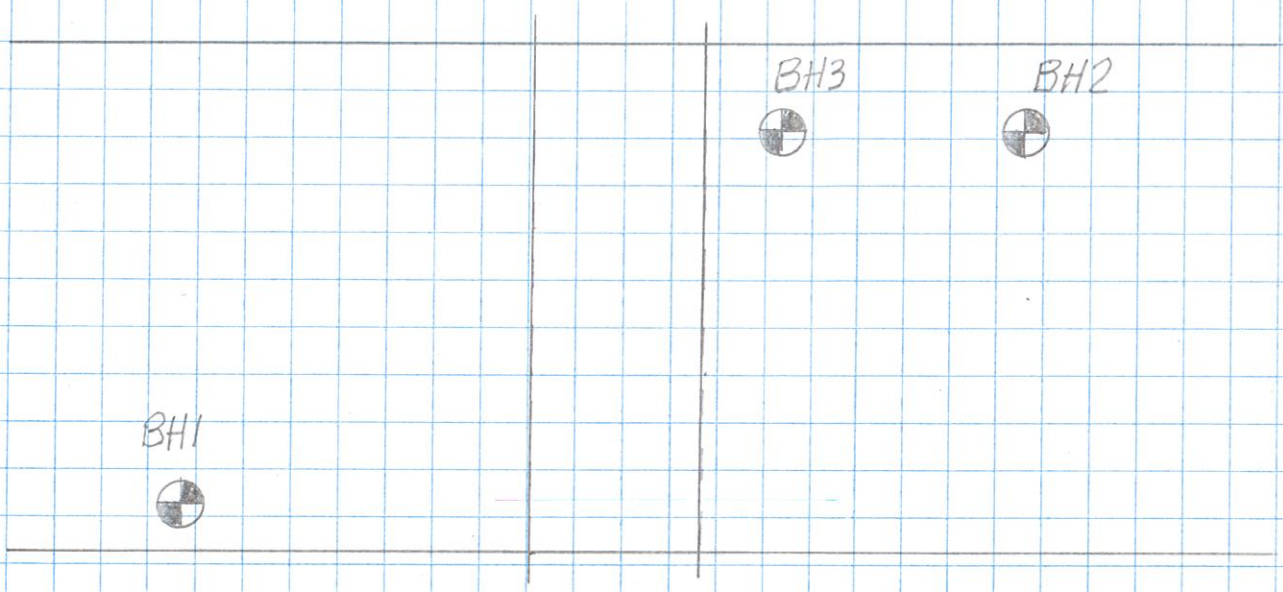

St. Lawrence Testing
Report 18C
September 2018
Scale 1:100

